



**Construction Update
for the
Citizens Advisory Committee**

September 13, 2011

Transbay Transit Center

TJPA





Transbay Transit Center

Demolition Update

- The demolition is complete. The contractor is finalizing their fence installation work and completing a short punchlist. The demolition equipment has been demobilized. All areas are available to the Webcor/Obayashi Team. The following are some demolition highlights:
 - Nearly 55,000 craft hours completed without accident or injury.
 - 92,000 cubic yards of concrete recycled, enough to fill 28 Olympic swimming pools.
 - 15,000,000 pounds of steel recycled.
 - Over 2 miles of elevated bus ramps demolished.



Transbay Transit Center

Construction Update – Utility Relocation Work

- Utility Relocation Packages

- **TG04.3 – Water Relocation on Howard and Beale Streets.** Water installation is complete. Demolition and capping of abandoned utilities is complete. The pavement restoration will be completed by the end of September.
- **TG04.6 – Sewer and Sludge Relocation on Beale Street.** Sewer and sludge work on Beale Street is 90% complete. The sludge line has been completed. Demolition and capping of the abandoned utilities will be completed by the end of September with the exception of Mission Street which will be completed later in the fall. Final pavement restoration on Beale will be completed by the end of September.
- **TG04.5.1 – Water and Sewer Relocation and Joint Trench on Minna Street.** Final pavement restoration at Minna Street was completed on June 18th. Demolition and capping of abandoned utilities on the north end of Fremont Street is complete. Investigative trenching across First Street, at Minna, remains un-restored and will be completed by the end of September.
- **TG04.1 – Water and Sewer Relocation Natoma and Fremont Streets.** Water installation, including pavement restoration, has been completed. The sewer work is 95% complete on Fremont Street, completion is anticipated the end of September.
- **TG04.4 – Water and Sewer Relocation on Natoma and First Streets.** Natoma and Second Streets Jack and Bore process is complete. The sewer work on Natoma Street is 95% complete, and will be completed by the end of September. Demolition and capping of abandoned utilities including final pavement restoration is to be completed by the end of September as well.
- **TG04.2 – AWSS on Mission Street.** The contract has been issued to M Squared and the submittal and procurement processes are underway.



Transbay Transit Center

Construction Update

- 301 Mission Street Temporary Wall
 - Complete.
 - Closeout in progress. TJPA is reviewing a final change request.
- Transit Center
 - Buttress, Shoring and Excavation (BSE)
 - BSE Construction
 - BBII continues pre-trenching in Zone 3 at Natoma Street and in Zones 1 and 2 along the north side at Minna Street. Pre-trenching along Natoma Street on the south side of Zones 1 and 2 has also just begun.
 - The CDSM Shoring wall test sections were completed in both the east and west ends of the project. The test panels have been cored and the core samples tested to confirm adequate strength was achieved. Both test wall sections have been approved.
 - BBII has completed the CDSM shoring wall along the north and south sides of Zone 4 and will be completing the east end of Zone 4 this month.
 - BBII continues to use the central section of the former terminal building for the fabrication of shoring steel for use in the shoring wall.
 - The buttress shaft drilling operation has mobilized into Zone 4 and drilling operations are scheduled to begin this week.



Transbay Transit Center

East Section Progress (Zone 4)



End of June 2011



End of August 2011



Transbay Transit Center

Central and West Sections Progress



End of June 2011



End of August 2011



Transbay Transit Center

Demolition Complete and Final Archeologist Pit Underway



End of August 2011





Transbay Transit Center

Final Building Demolition



60 Tehama



564 Howard




568 Howard



Transbay Transit Center

BSE Timeline Summary

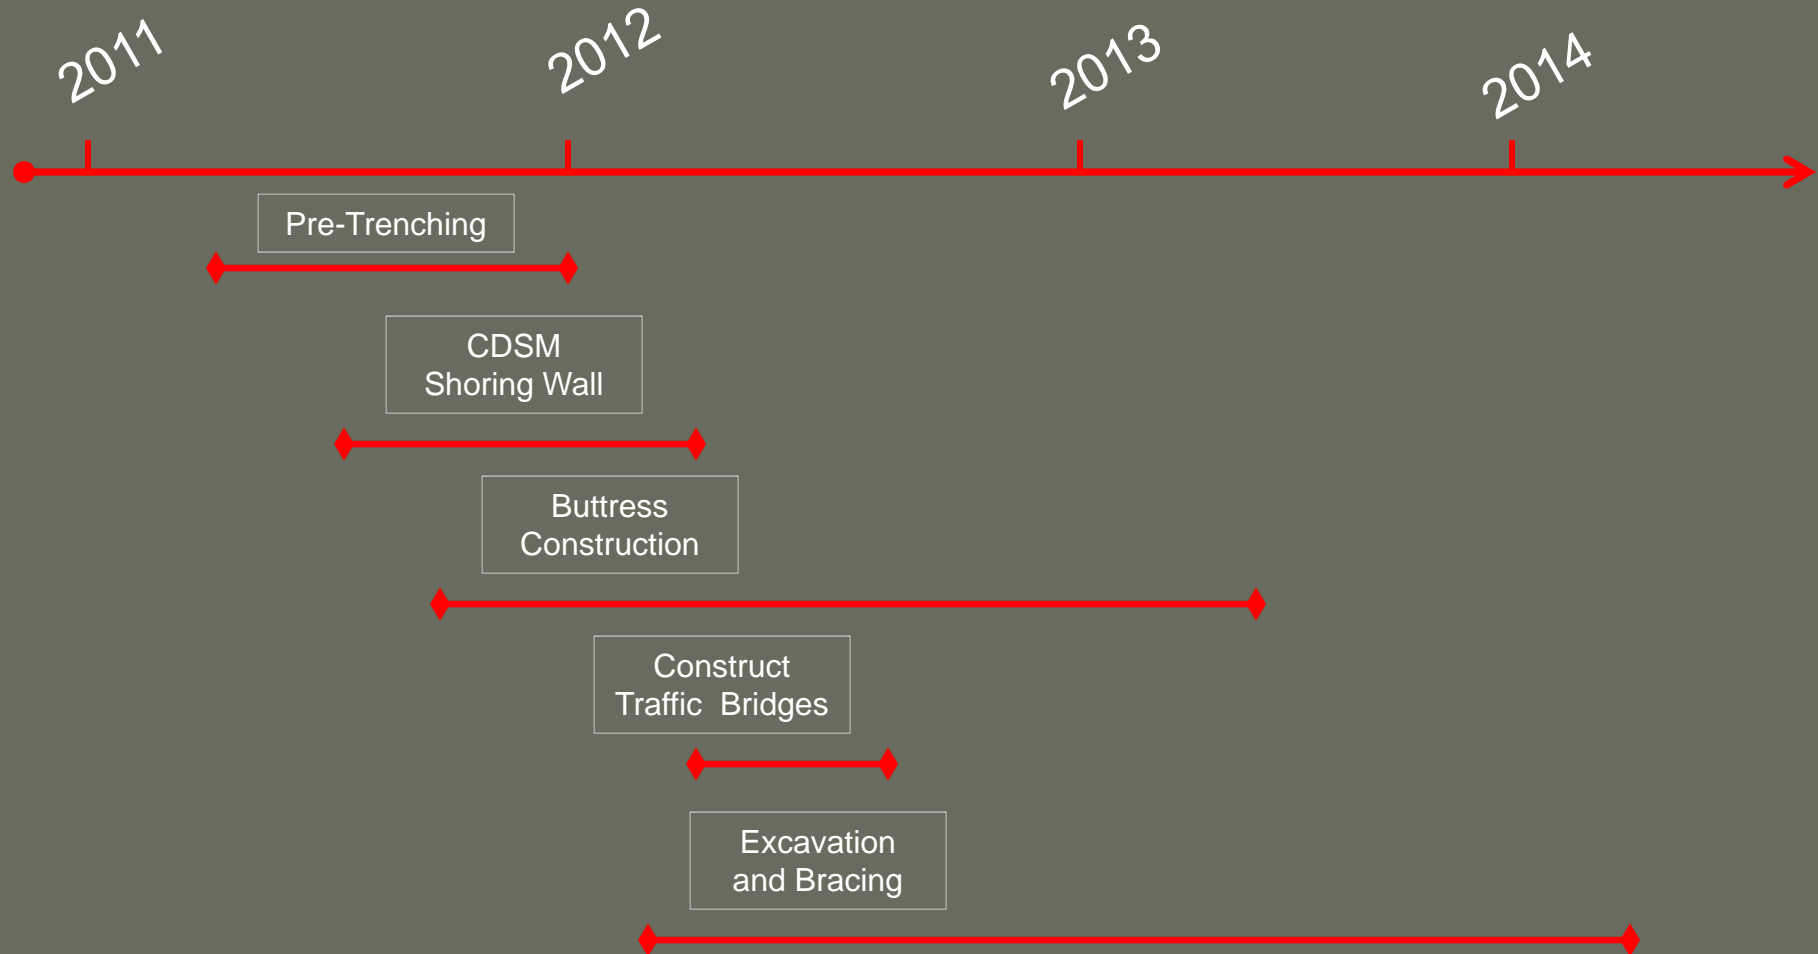



Transbay Transit Center

August 31, 2011 BSE Status






2011

2012

2013

2014



- CDSM Complete 
- CDSM in Progress 
- Pre-trenching Complete 
- Pre-trenching in Progress 
- Buttress Work in Progress 



Transbay Transit Center

Pre-Trenching





Transbay Transit Center

CDSM Operation in Zone 4





Transbay Transit Center

Buttress Equipment Mobilized





Transbay Transit Center

Quality Control



Instrumentation

CDSM Shoring Wall Cores





Transbay Transit Center

Utility Relocation





Transbay Transit Center

Utility Relocation





Transbay Transit Center

Questions?
