



CAC Construction Update

March 13, 2012

Transbay Transit Center

TJPA





Transbay Transit Center


Update

- Over 230,000 craft hours completed to date, over 20,000 craft hours completed this period.
- Completed 10 shafts this period, average of 2.5 shafts per week, total of 50 shafts completed to date.
- Started pin pile supports for the Trestle Bridge to be installed in Zones 1 and 2.
- PG&E Phase II infrastructure complete on Fremont Street, Verizon Phase II cutovers complete on First Street.
- Preparations are underway for the completion of the CDSM wall at First Street and the installation of the Traffic Bridge over Memorial Day Weekend.
- One recordable safety incident this period, sprained ankle, worker returned to work.



Transbay Transit Center

BSE Timeline Summary

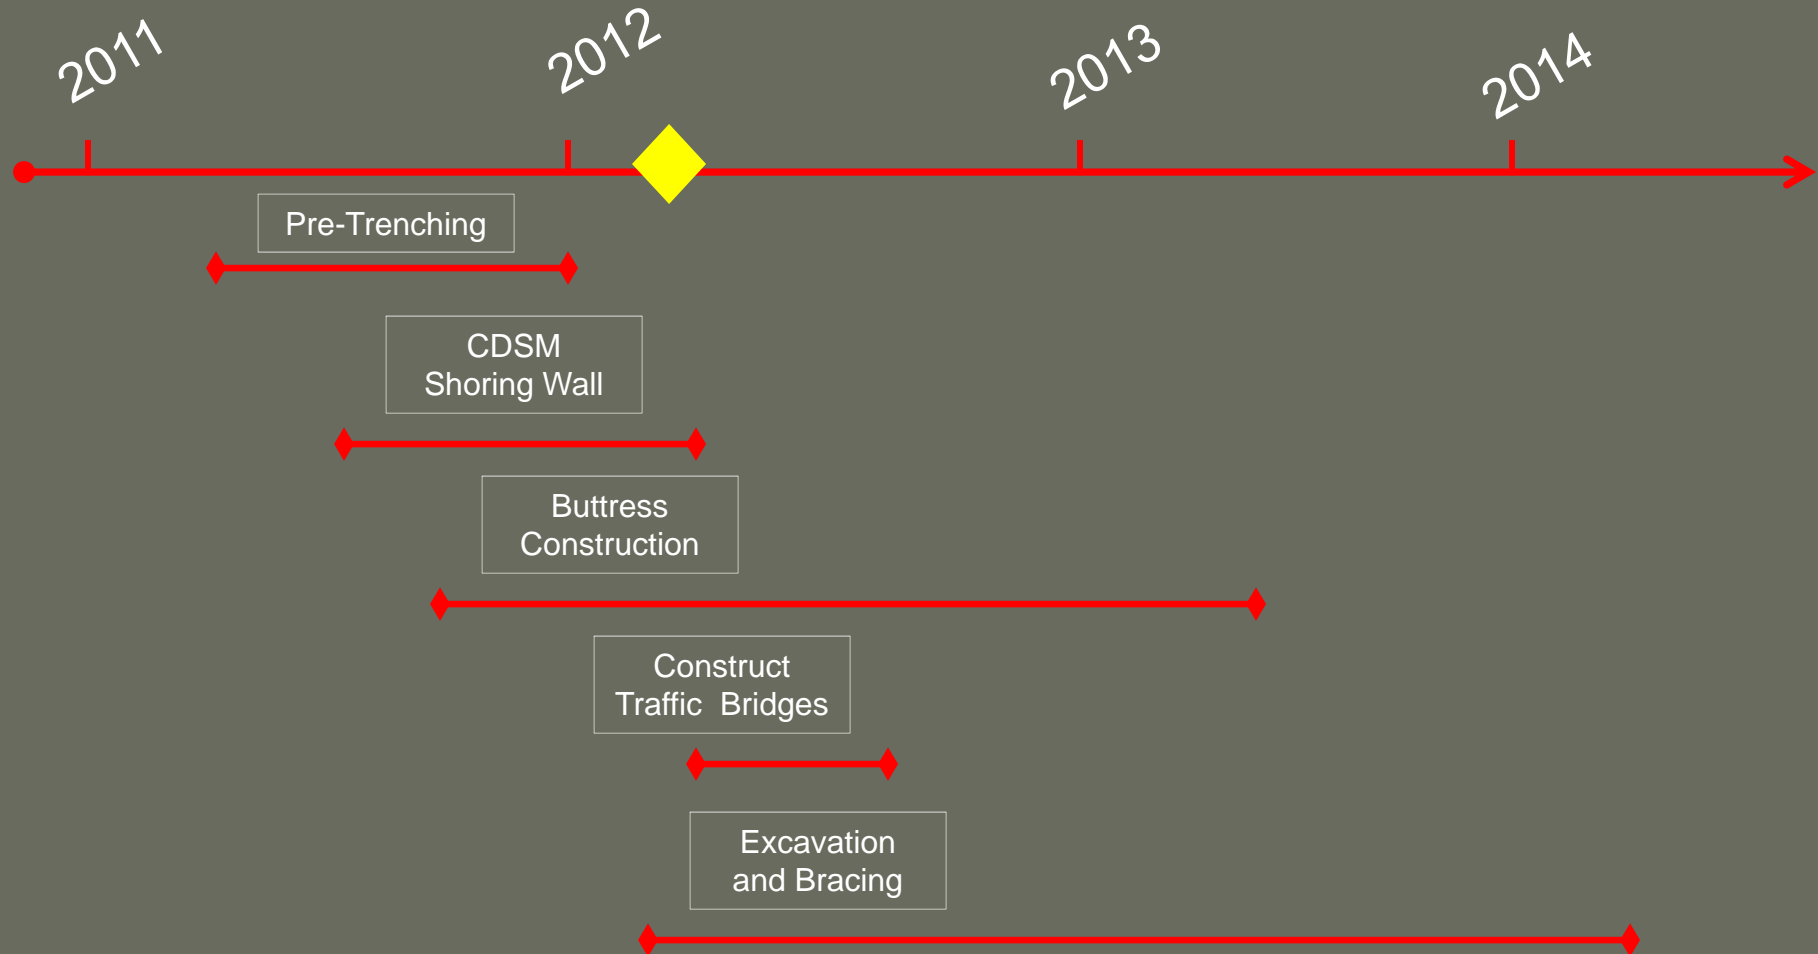



Transbay Transit Center


March 1, 2012 Site Status

2011

2012

2013

2014

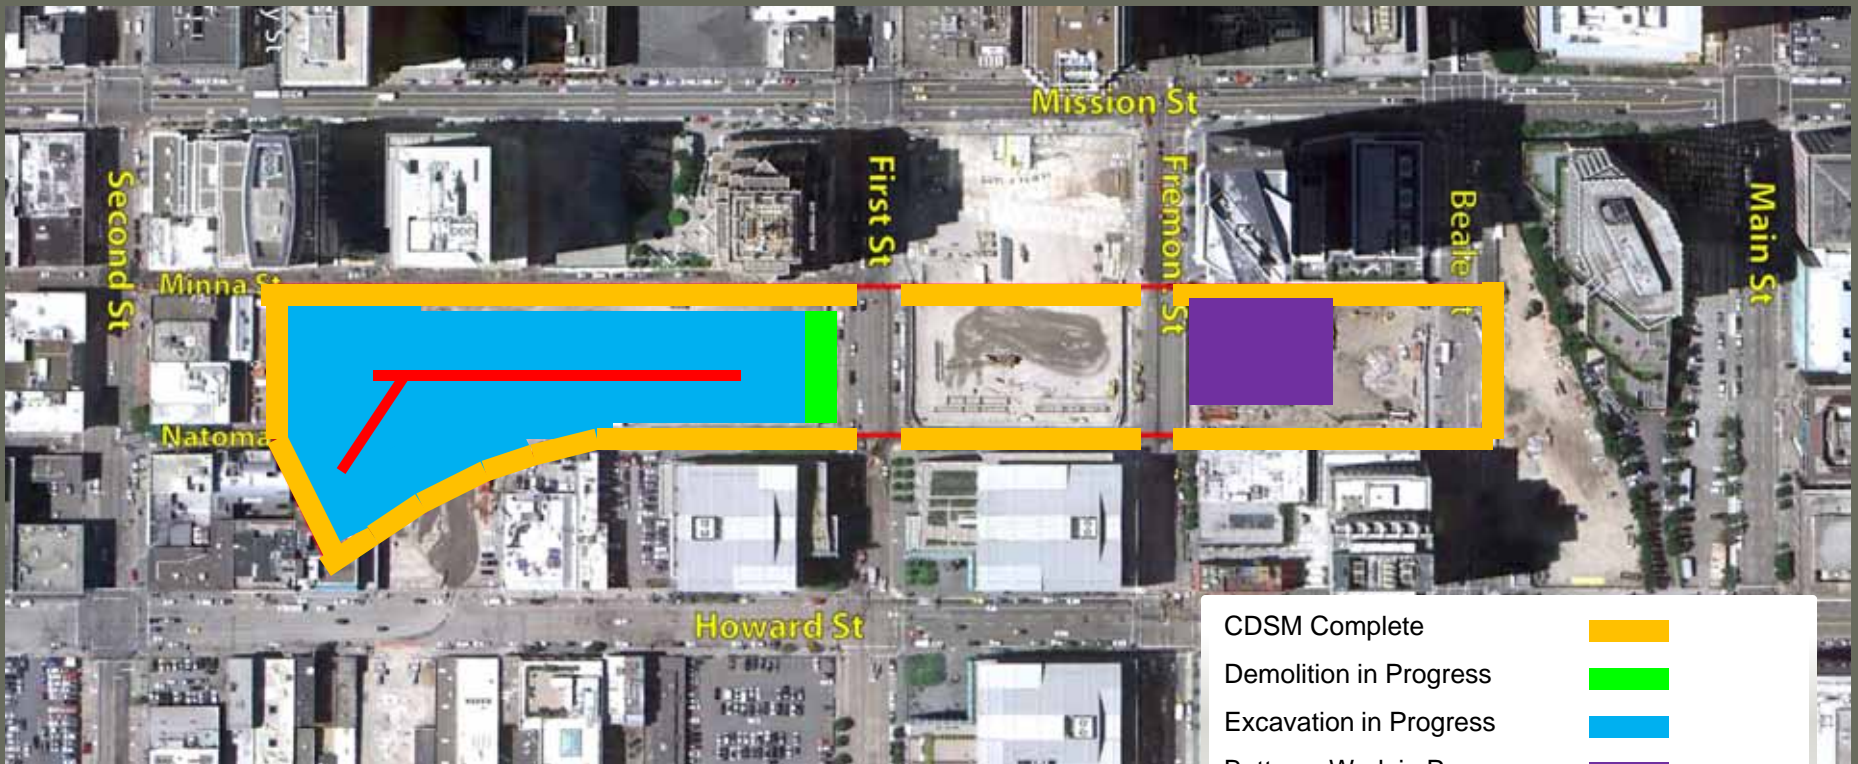

CDSM Complete	
Demolition in Progress	
Excavation in Progress	
Buttress Work in Progress	
Trestle Piles in Progress	



Transbay Transit Center

East Section Progress (Zone 4)



End of January 2012




End of February 2012



Transbay Transit Center

Buttress Progress

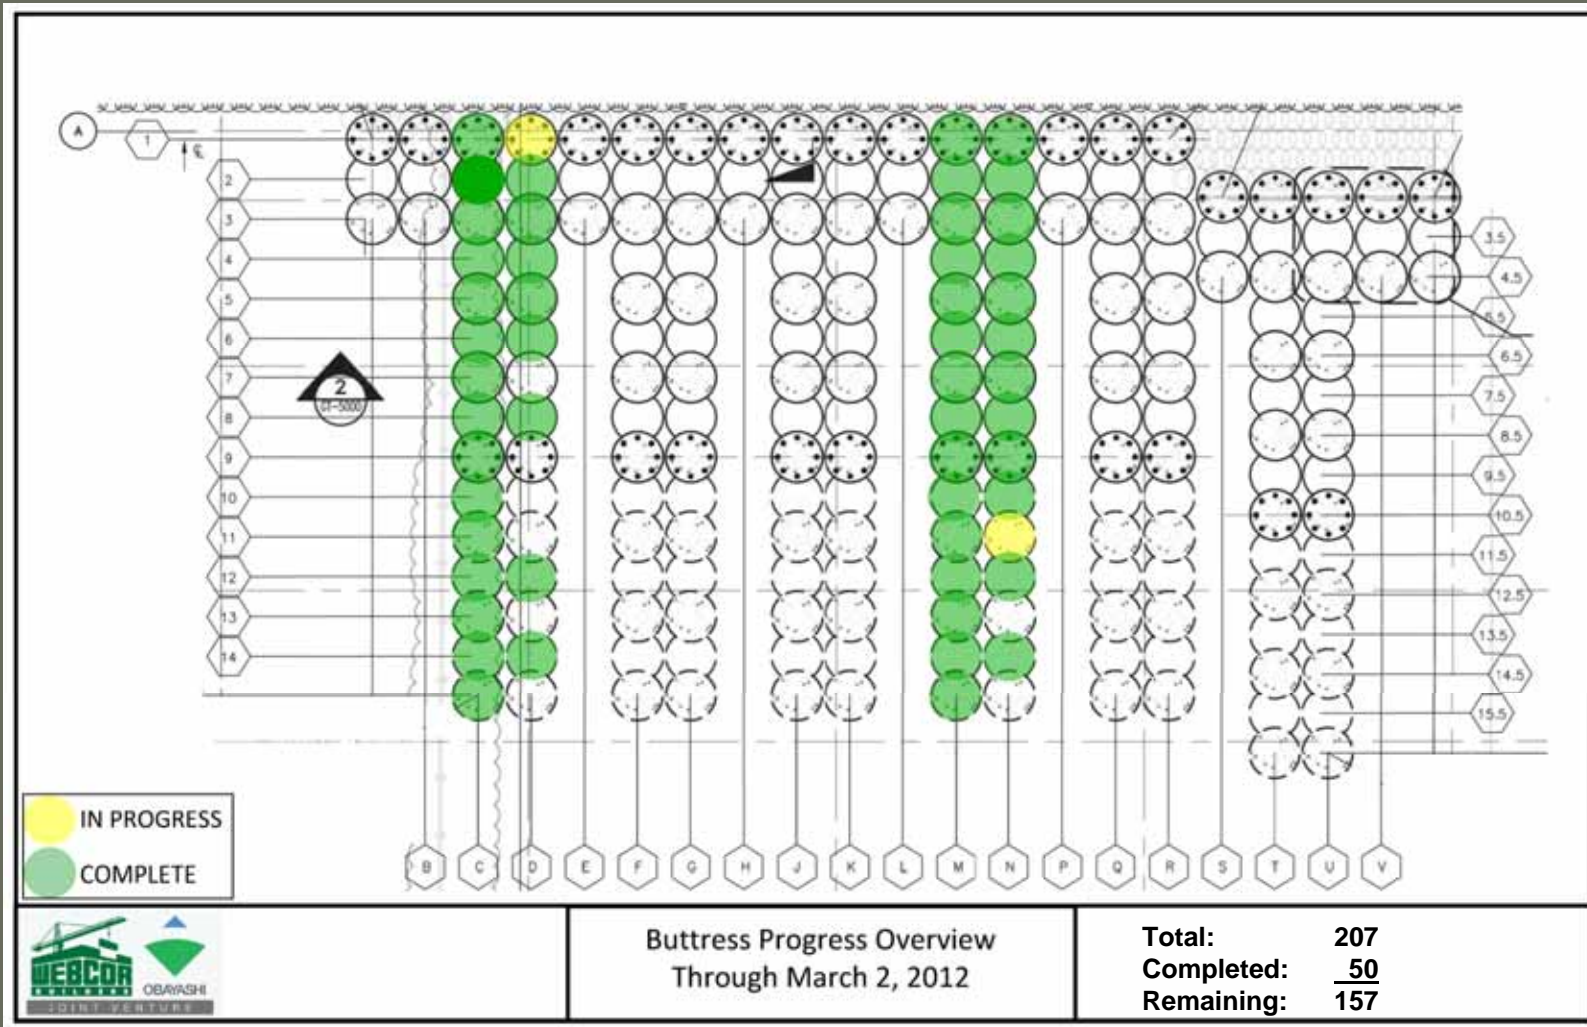



Transbay Transit Center

Buttress Progress





Transbay Transit Center

Buttress Progress – New Equipment



New Rotator arrived onsite this period





Transbay Transit Center

Central and West Sections Progress



End of January 2012



End of February 2012



Transbay Transit Center

Excavation – Zones 1 and 2





Transbay Transit Center

Excavation – Zones 1 and 2; Pin Pile Placement





Transbay Transit Center

Excavation – Zones 1 and 2; Internal Bracing





Transbay Transit Center

Utility Relocation - Continued Potholing for AWSS





Transbay Transit Center

Phase II PG&E Infrastructure – Completing Fremont Street





Transbay Transit Center

Phase II Utilities – Verizon on First Street





Transbay Transit Center

Questions?
